

New Campus Ardingly Astana

Construction progress and
key implementation
milestones as of 28 September 2026





Construction and installation works schedule



№	Name	Completion date	June 26	July 26	August 26	Percentage completed
1	Preparatory works					100%
2	Substructure works (zero cycle)					100%
3	Monolithic works					100%
4	Walls and partitions					100%
5	Roofing, metal structures					100%
6	Window units					100%
7	On-site utility networks					100%
8	Engineering systems					95%
9	Interior finishing					95%
10	Facade works					100%
11	Landscaping and site improvement					75%
12	Equipment and furnishing					100%
13	Commissioning and handover					0%
14	Organization of the educational process					100%





September 25, 2026



June 10, 2026






September 25, 2026



June 10, 2026

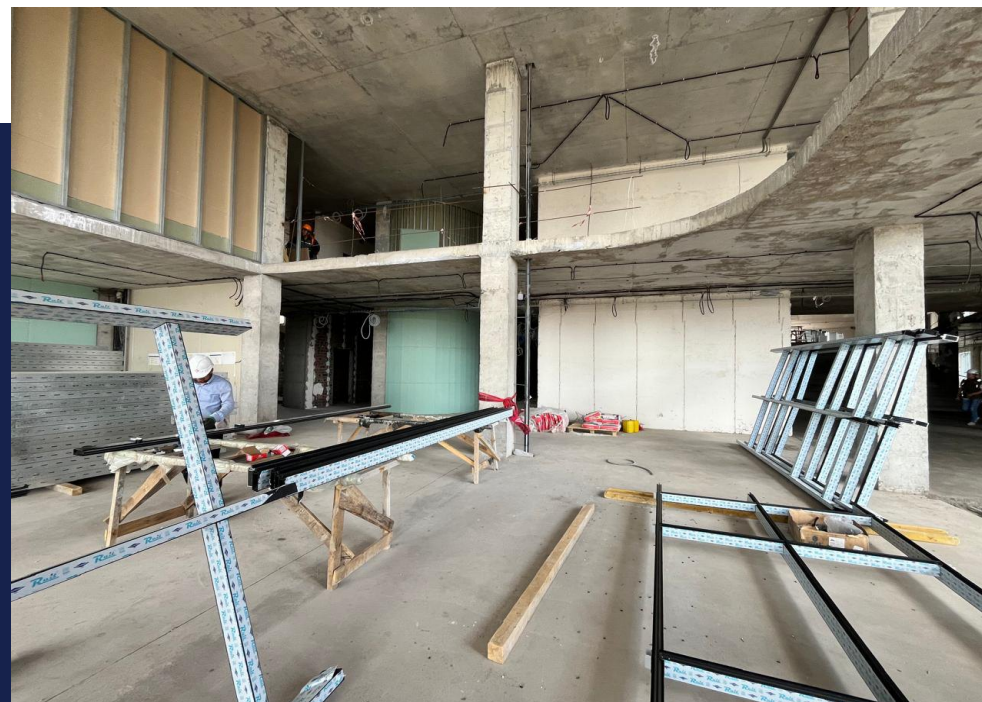



September 25, 2026



June 10, 2026





September 25, 2026



June 10, 2026





June 10, 2026




September 25, 2026





September 25, 2026

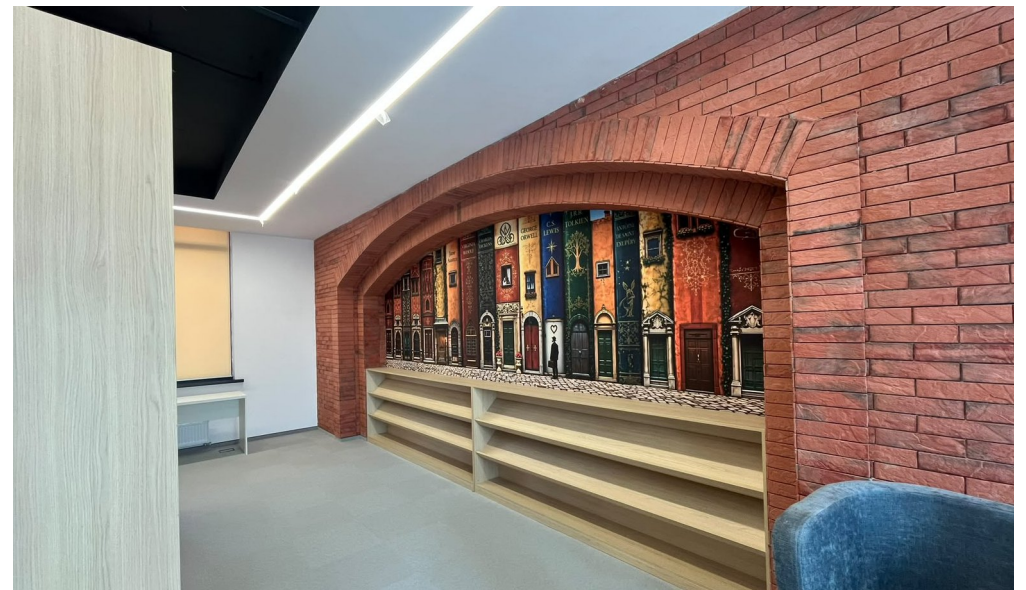



September 25, 2026





Thank you for your attention
